go Transit Authority
General Operations Division
Transportation Department

Service bulletin

Rail			Bus		
	file	X		file	
	post	X		post	
	spl.	X		other	

S229-81

R.C.O.O. #16811

TO: All Concerned, Rail

SUBJECT: Single Track Movement, Ravenswood Route

EFFECTIVE: Friday, August 21, 1981 - 2100 Hours to
Monday, August 24, 1981 - 0500 Hours

The northbound track between Western Avenue and Kimball Terminal will be out of service from 2100 hours on Friday, August 21, 1981 to 0500 hours on Monday, August 24, 1981.

Phase I - Friday, August 21, 1981 - 2100 Hours to
Saturday, August 22, 1981 - 0700 Hours

On Friday, August 21, 1981 through Saturday, August 22, 1981 the Ravenswood Route will operate according to the following special supplement.

SINGLE TRACK ZONE

A single track zone will be in effect on the southbound track between Kimball Terminal and Western Avenue.

WORK TO BE DONE

A contractor will cut and throw the rail on the northbound track at the Rockwell Bridge, Ravenswood Route.

ROUTING

Northbound Normal to clear right-hand crossover at Western Avenue. Pilot will board rear of train and pull back the train through the crossover to the southbound track. On orders of the pilot and proper signals, motormen will operate northbound on the southbound track to the interlocking plant at Kimball Terminal.

Southbound Normal on orders of pilot.

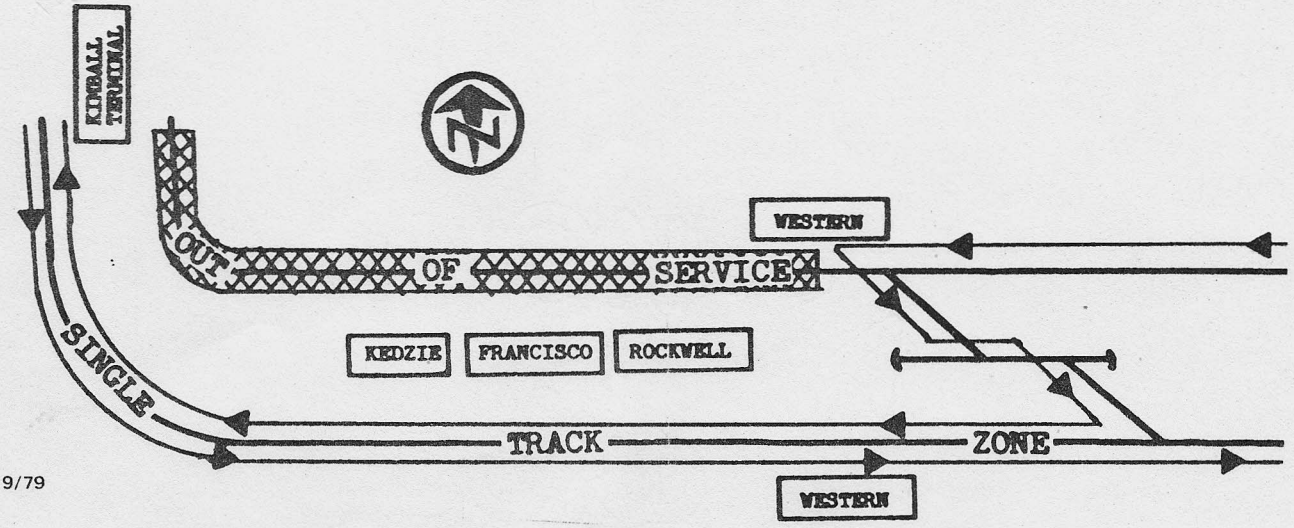

T 400 9/79
